BEALL AVENUE STREETSCAPE / PHASE 1
FOR
THE CITY OF WOOSTER

Description	Original Duration	Target Start	Target Finish
CLEARING AND GRUBBING	2d	12MAR09	13MAR09
SANITARY SEWERS	1d	13MAR09	13MAR09
STORM SEWERS	25d	16MAR09	17APR09
WATERMAINS	17d	20APR09	12MAY09
WATER TIE INS / SERVICES	9d	13MAY09	25MAY09
WALL EXCAVATION	7d	15MAY09	25MAY09
WALL FOOTERS / CORE WALL	9d	26MAY09	05JUN09
ELECTRIC CROSSOVERS	7d	05JUN09	15JUN09
LIGHT POLE FOUNDATIONS	11d	12JUN09	26JUN09
EXCAVATION / REMOVALS	36d	23JUN09	11AUG09
UNDERDRAINS	9d	02JUL09	14JUL09
CURBING INSTALLATION	11d	08JUL09	22JUL09
BASE ASPHALT	6d	23JUL09	30JUL09
CONCRETE CROSSOVERS	11d	24JUL09	07AUG09
DRIVE APRONS / SIDEWALKS	15d	10AUG09	28AUG09
LIGHT POLE INSTALLATION	8d	12AUG09	21AUG09
PAVERS	15d	14AUG09	03SEP09
STONEWORK ON WALLS	15d	10SEP09	30SEP09
LANDSCAPING	12d	18SEP09	05OCT09
PAVING / STRIPING	7d	01OCT09	09OCT09

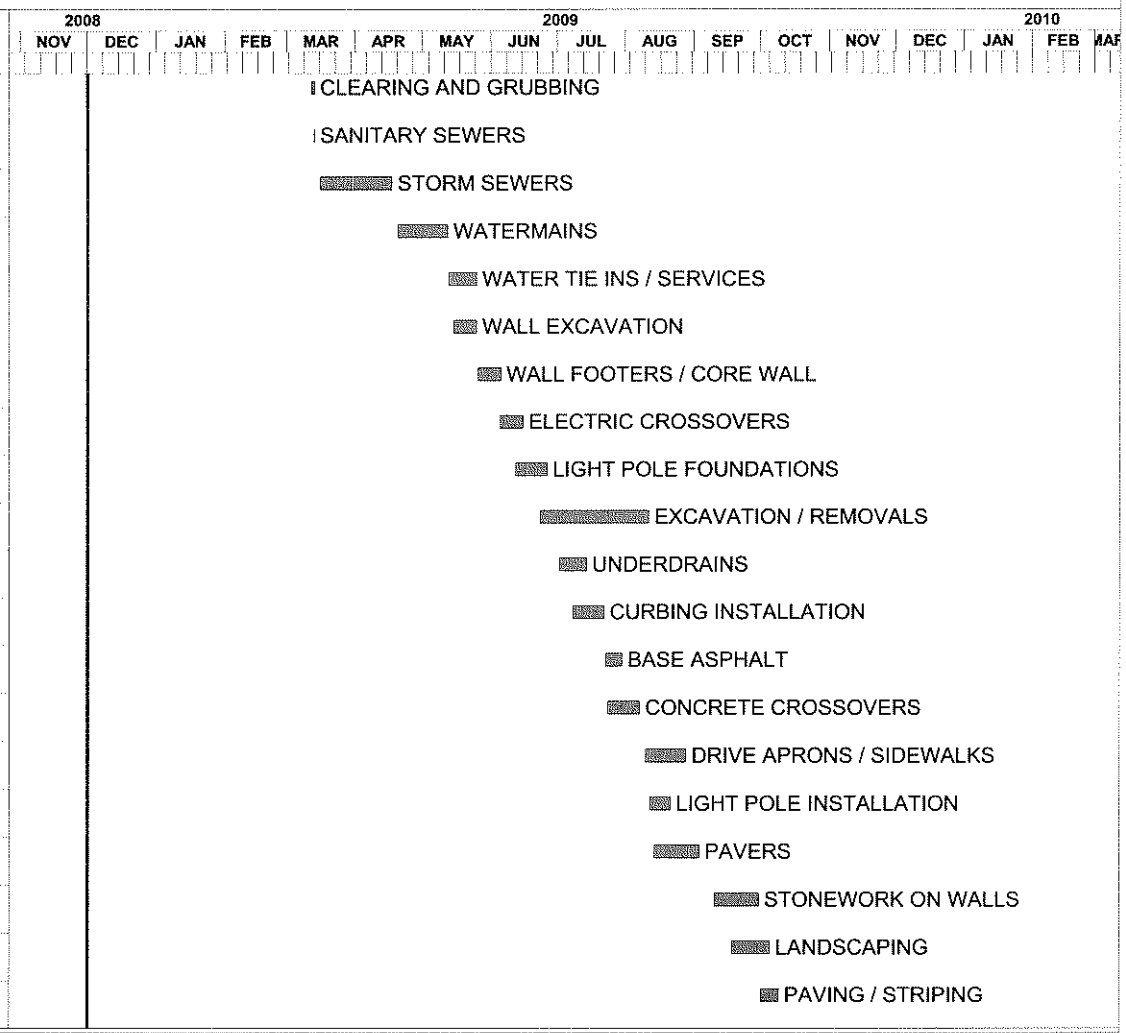

		Date	Revision	Checked	Approved
Start date	03NOV08				
Finish date	21JAN09				
Data date	01DEC08				
Run date	17FEB09				
Page number	1A				

© Primavera Systems, Inc.

NORTHSTAR ASPHALT, INC.
BEALL AVENUE STREETSCAPE / PHASE 1

BEALL AVENUE STREETSCAPE / PHASE 2
FOR
THE CITY OF WOOSTER

Description	Original Duration	Target Start	Target Finish
CLEARING AND GRUBBING	2d	15JUN09	16JUN09
SANITARY SEWER SLIPLINING	12d	15JUN09	30JUN09
STORM SEWERS	23d	22JUN09	22JUL09
WATERMAINS	8d	23JUL09	03AUG09
WATER TIE INS / SERVICES	6d	04AUG09	11AUG09
WALL EXCAVATION	7d	04AUG09	12AUG09
WALL FOOTERS / CORE WALL	10d	13AUG09	26AUG09
ELECTRIC CROSSOVERS	7d	24AUG09	01SEP09
LIGHT POLE FOUNDATIONS	8d	02SEP09	11SEP09
EXCAVATION / REMOVALS	34d	24AUG09	08OCT09
UNDERDRAINS	8d	01SEP09	10SEP09
CURBING INSTALLATION	11d	07SEP09	21SEP09
BASE ASPHALT	6d	18SEP09	25SEP09
CONCRETE CROSSOVERS	9d	23SEP09	05OCT09
DRIVE APRONS / SIDEWALKS	16d	06OCT09	27OCT09
LIGHT POLE INSTALLATION	8d	07OCT09	16OCT09
PAVERS	14d	21OCT09	09NOV09
STONEWORK ON WALLS	6d	10NOV09	17NOV09
LANDSCAPING	12d	19OCT09	03NOV09
PAVING / STRIPING	7d	02NOV09	10NOV09

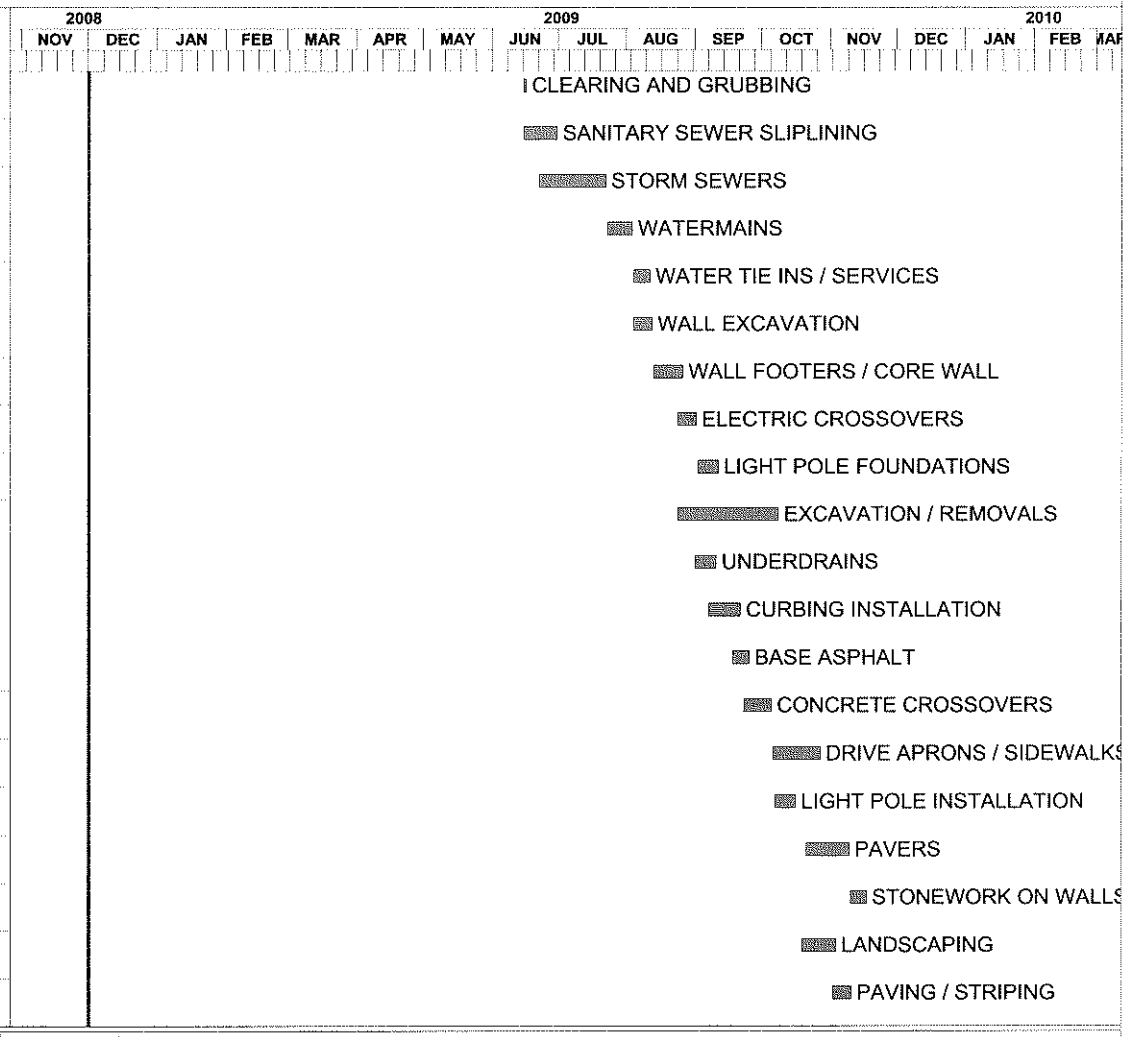

		Date	Revision	Checked	Approved
Start date	03NOV08				
Finish date	19JAN09				
Data date	01DEC08				
Run date	17FEB09				
Page number	1A				

© Primavera Systems, Inc.

NORTHSTAR ASPHALT, INC.
BEALL AVENUE STREETSCAPE / PHASE 2

BEALL AVENUE STREETSCAPE / PHASE 3
FOR
THE CITY OF WOOSTER

Description	Original Duration	Target Start	Target Finish
CLEARING AND GRUBBING	12d	15DEC08	31DEC08
SANITARY SEWERS	32d	10DEC08	26JAN09
WATERMAINS	19d	27JAN09	20FEB09
STORM SEWERS	15d	23FEB09	13MAR09
WATER TIE INS / SERVICES	6d	13MAR09	20MAR09
WALL EXCAVATION	6d	16MAR09	23MAR09
WALL FOOTERS / CORE WALL	12d	24MAR09	08APR09
ELECTRIC CROSSOVERS	9d	16MAR09	26MAR09
LIGHT POLE FOUNDATIONS	14d	27MAR09	15APR09
EXCAVATION / REMOVALS	45d	06APR09	05JUN09
UNDERDRAINS	14d	30APR09	19MAY09
CURBING INSTALLATION	10d	04MAY09	15MAY09
BASE ASPHALT	8d	08MAY09	19MAY09
CONCRETE CROSSOVERS	6d	11MAY09	18MAY09
DRIVE APRONS / SIDEWALKS	22d	18MAY09	16JUN09
LIGHT POLE INSTALLATION	13d	15MAY09	02JUN09
PAVERS	17d	11JUN09	03JUL09
STONEWORK ON WALLS	8d	06JUL09	15JUL09
LANDSCAPING	14d	09JUL09	28JUL09
PAVING / STRIPING	7d	21JUL09	29JUL09

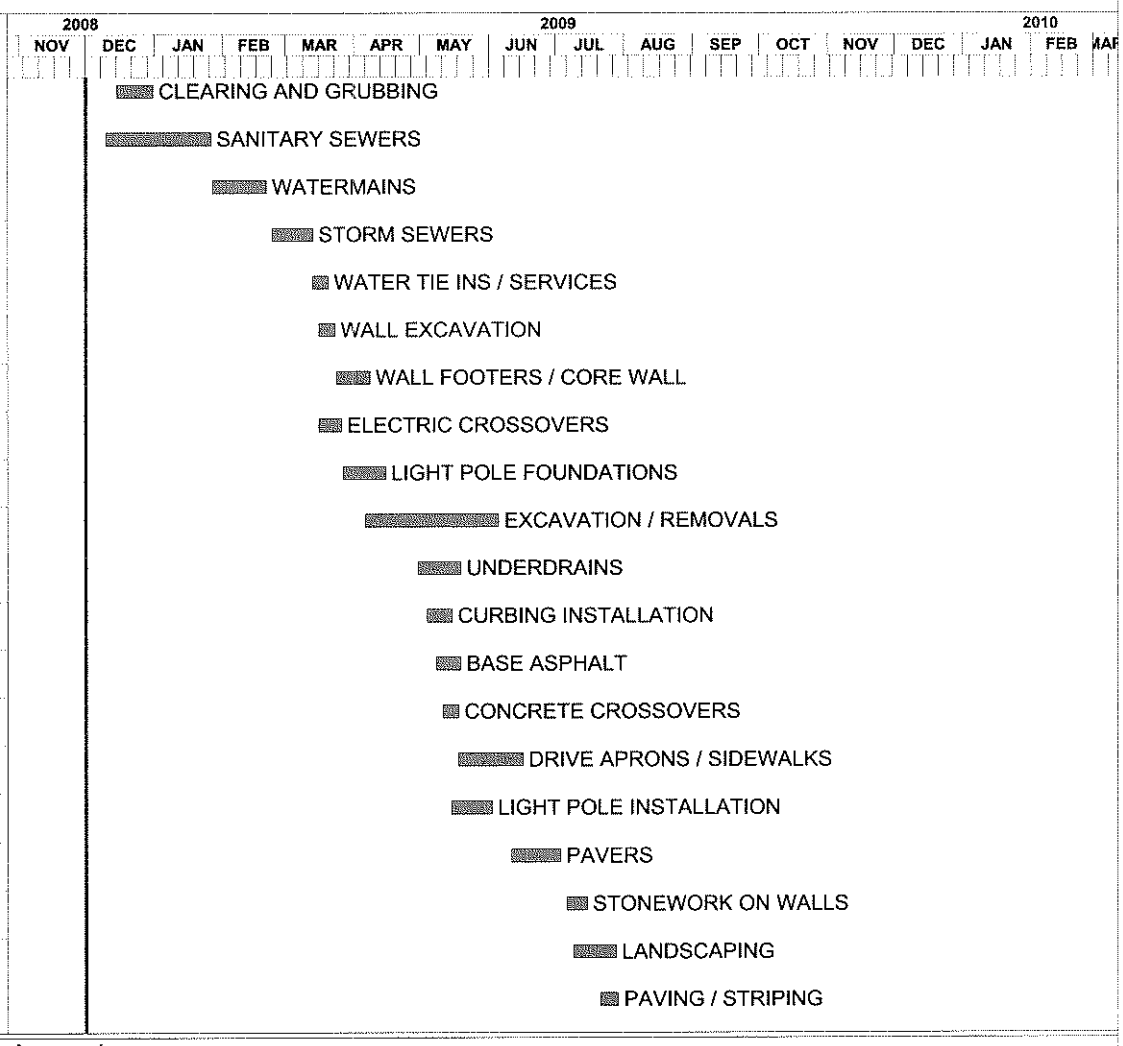

		Date	Revision	Checked	Approved
Start date	03NOV08				
Finish date	03FEB09				
Data date	01DEC08				
Run date	17FEB09				
Page number	1A				

© Primavera Systems, Inc.

NORTHSTAR ASPHALT, INC.
BEALL AVENUE STREETSCAPE / PHASE 3
